Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
Ajo Way					
Design					
1000	Design	100	38	02APR07A	17AUG07
Utility Construction					
1010	Utility Construction	75	75	16JUL07	26OCT07
Roadway Construction					
1020	Roadway Construction	97	97	15OCT07	26FEB08
Kinney along Center and South					
Design					
1030	Design	90	43	23APR07A	24AUG07
Utility Construction					
1040	Utility Construction	92	92	13AUG07	18DEC07
Roadway Construction					
1050	Roadway Construction	122	122	24OCT07	10APR08
Ajo/Kinney Intersection					
Design					
1060	Design	95	88	18JUN07A	26OCT07
Utility Construction					
1070	Utility Construction	45	45	07NOV07	08JAN08
Roadway Construction					
1080	Roadway Construction	58	58	07MAR08	27MAY08
Kinney north of Center, Sarasota, and Bopp					
Design					
1090	Design	95	95	02JUL07	09NOV07
Utility Construction					
1100	Utility Construction	65	65	09JAN08	08APR08
Roadway Construction					
1110	Roadway Construction	120	120	04APR08	18SEP08
EAMR					
1120	EAMR	123	81	30APR07A	17OCT07

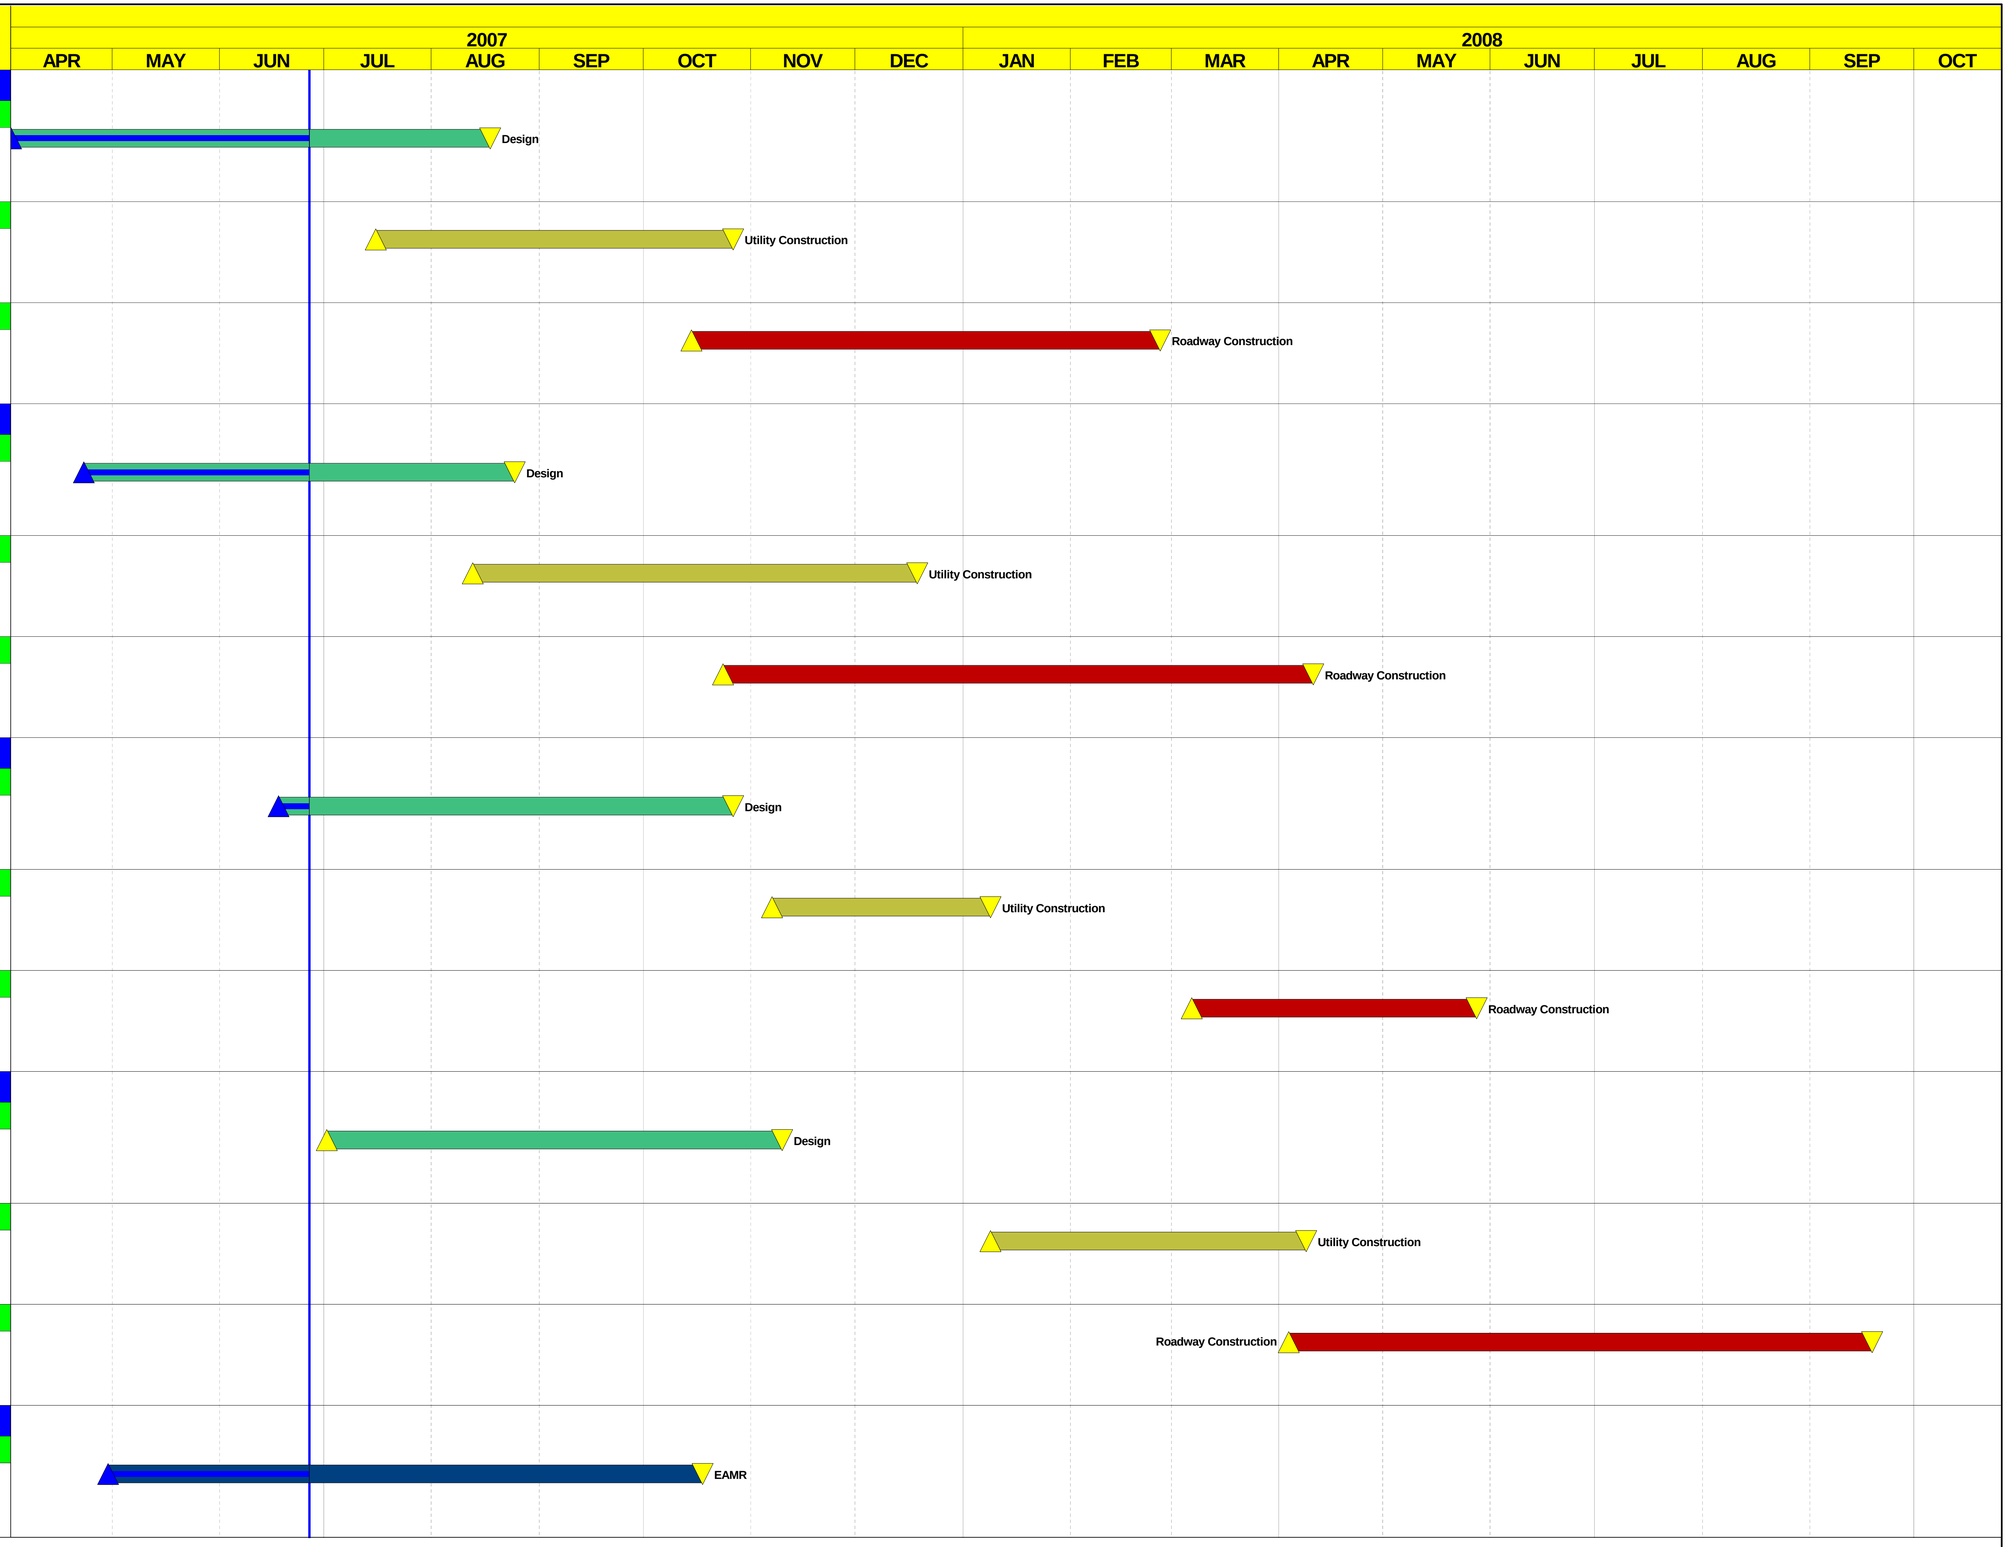

Start Date	02APR07
Finish Date	18SEP08
Data Date	27JUN07
Run Date	22JUN07 16:26

Early Bar
Progress Bar

AK04

Sheet 1 of 1

Ajo/Kinney May Update

Classic Schedule Layout

Date	Revision	Checked	Approved

© Primavera Systems, Inc.
